

DRY LAKE HILLS SPA & PROJECT UPDATE




Flagstaff Watershed Protection Project

SPA: DLH Preparation Phase I & II

- \$654,761.02 (NTE) for required preparation work (tree marking, inventory, mapping, etc) throughout entire DLH area;
- No general administrative costs included;
- Schedule is to begin cutting Phase I by summer 2016: ≈ 390 acres of hand thinning and 690 acres of mechanical harvesting;
- Phase II cutting will be initiated in 2017/18: ≈ 3,800 acres involving all treatment methods.

Location: Phase I only

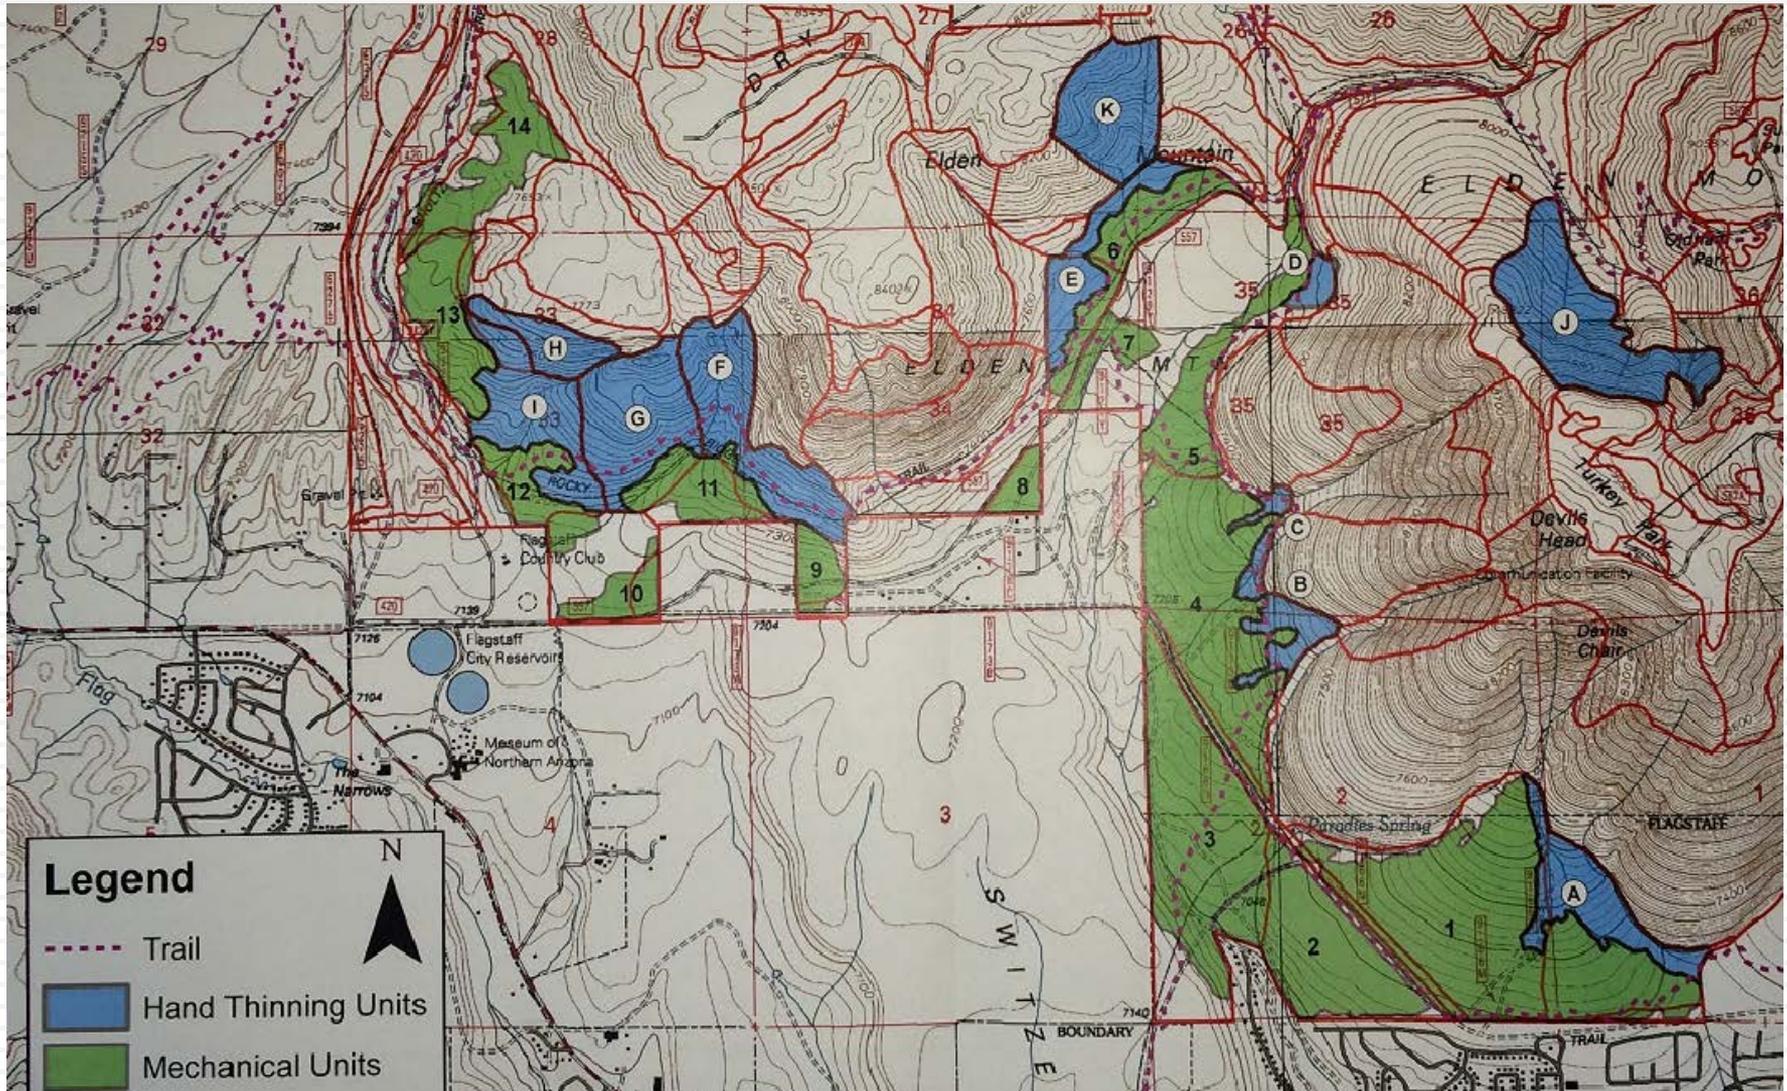

Project Update: Key Benchmarks

- Leverage funds: \$2.57M
 - ❖ Three years (2-13-15),
 - ❖ \$1.82M has been from USFS
- CY15:
 - ❖ Completed 16-of-23 plus 9 others,
 - ❖ Of 7 not yet completed, 4 underway and 3 moved to FY16
- To-date, across all jurisdictions:
 - ❖ 1,710 acres of cutting (hand thinning & mechanical harvesting),
 - ❖ 215 acres of broadcast prescribed fire

Project Update: Public Outreach

□ FWPP Communications Team

□ Developing plan

❖ Strategic

- Identifying and engaging key community networks and influential persons (ex: Yes on 405 committee members, Education centers, Environmental groups, arts community, others),
- Semi-annual media updates
- Community Forest & Watershed Academy,
- Business constituents (ex: beersheds, bedsheds, others)

Project Update: Public Outreach

❖ Tactical

➤ Website updates, Flickr photo account, YouTube, etc

➤ Media

➤ Planned

<u>EVENTS</u>
<ul style="list-style-type: none">• Wildfire Preparedness Day• Harvesting Method Workshop• Firewise Community Landscape Contest• Festival of Science• Other
<u>FIELD TRIPS</u>
<ul style="list-style-type: none">• Elden Schulz Pass area• Mtn Shadows area• Observatory Mesa• Other

Questions?

Working to Prevent



Working to Create



www.flagstaffwatershedprotection.org

